NANDAN GSE · FY2026-27

The year, as the book stands today

Day 140 of 365. Everything delivered so far, plus every job on the board, comes to just over half the year's target.

SALES — ANTICIPATED

₹50.76 Cr

of ₹100.00 Cr target

51% of target

THROUGHPUT — ANTICIPATED

₹21.24 Cr

of ₹40.00 Cr target

53% of target

> **The book runs out in November.** 105 jobs, all of them dated between August and November — nothing after.

> **₹4.32 Cr is kitted and not moving.** Material bought, sitting on the floor, nothing earned against it.

> **59 of 105 jobs are escalated** — and it is the same cause on job after job.

delivered since 1 April + every job still on the board

SINCE 1 APRIL

Genie · as at 18-08-2026

What has actually gone out of the door

DELIVERED

₹17.18 Cr

61 jobs · ₹8.68 Cr throughput

PACE SAYS BY TODAY

₹38.36 Cr

140 of 365 days elapsed

BEHIND BY


₹21.18 Cr

running at 45% of the pace needed

REQUIRED RUN RATE FOR THE REST OF THE YEAR

₹11.20 Cr per month in sales, with a throughput of **₹4.23 Cr** per month

across the 225 days that remain

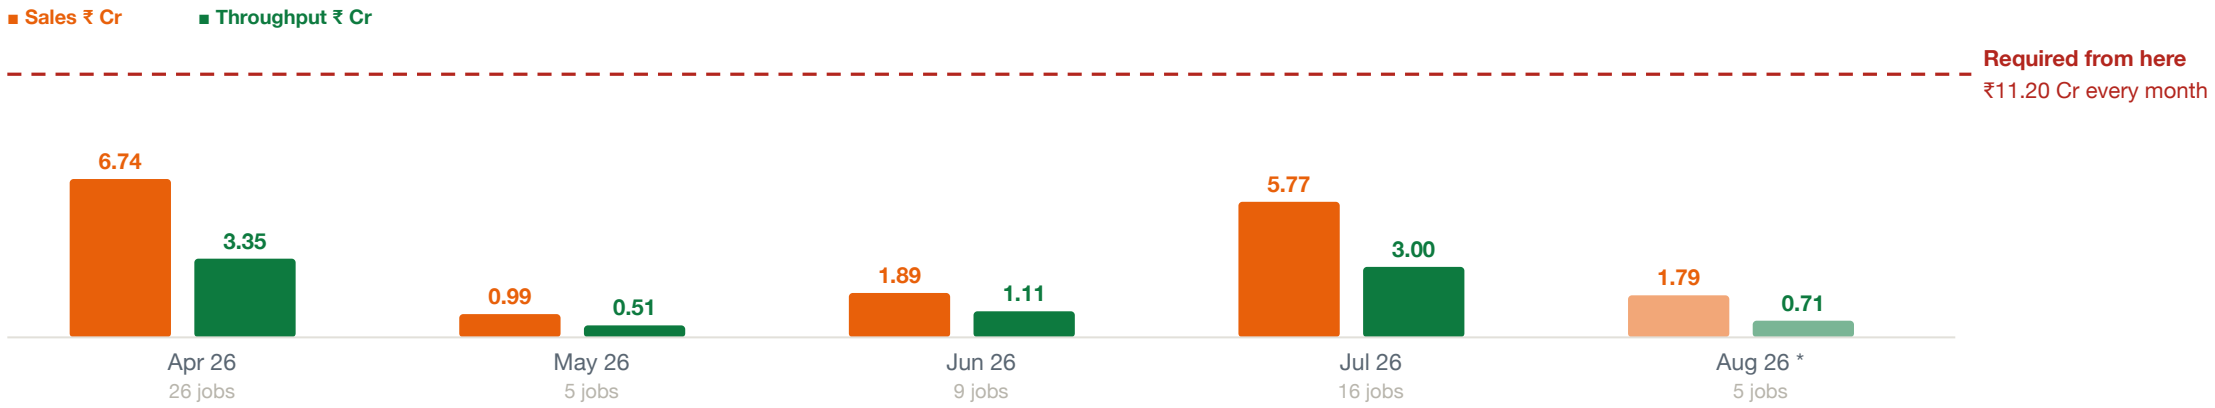


No month this year has reached the rate now required; the best of them, April, came to ₹6.74 Cr. ** Aug 26 is 18 days old, not a full month.*

THE ORDER BOOK

Genie · as at 18-08-2026

Everything on the board runs out in November

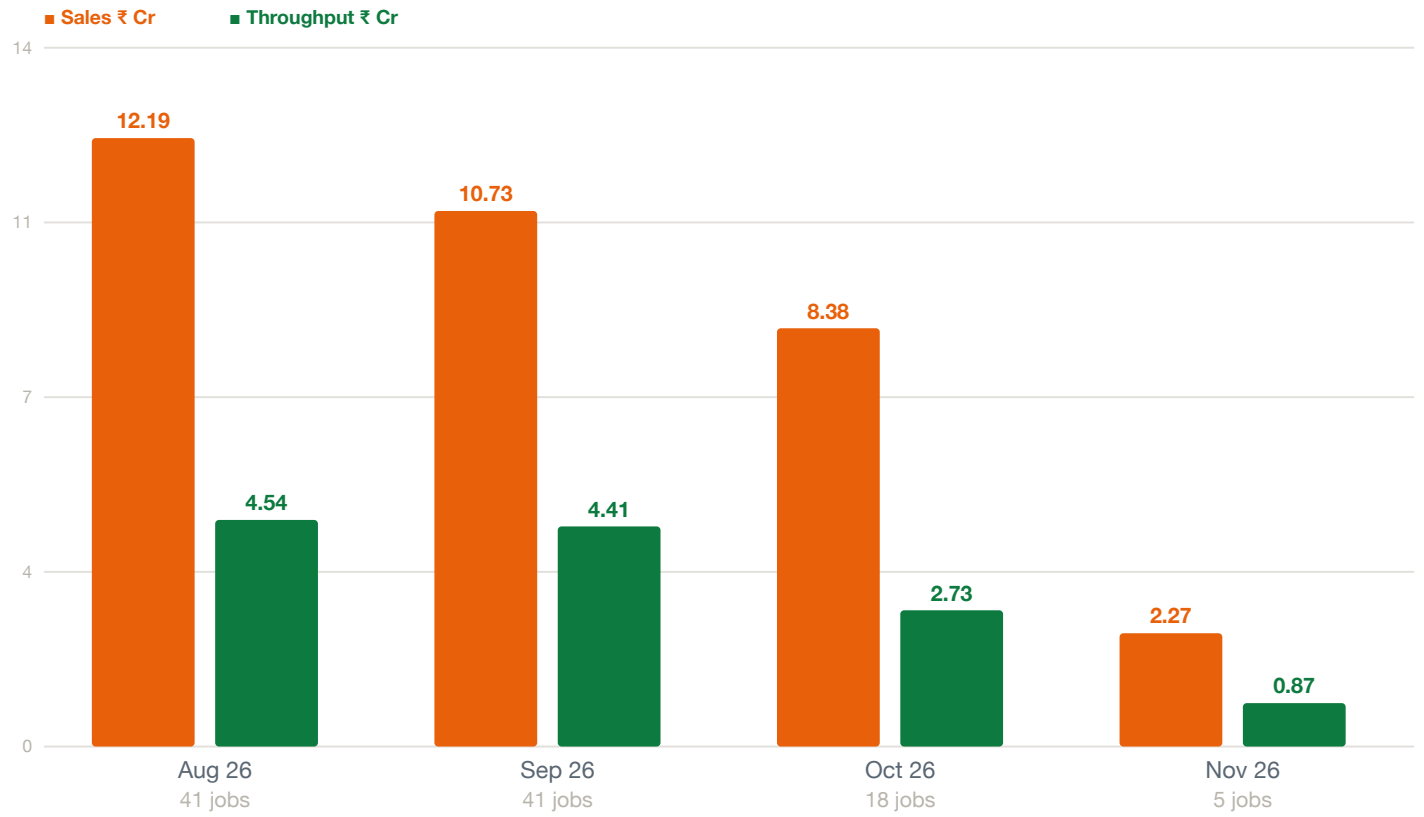

ON THE BOARD

105 jobs

₹33.58 Cr · ₹12.56 Cr throughput

all of it dated Aug–Nov

DEC ONWARDS

Nothing


Not one job on the book carries a delivery date after November.

This is not a delivery problem. Even built perfectly and on time, the current book cannot reach the target — the shortfall is orders, not output.

THE BOOK BY PRODUCT

Genie · as at 18-08-2026

What the 105 jobs actually are

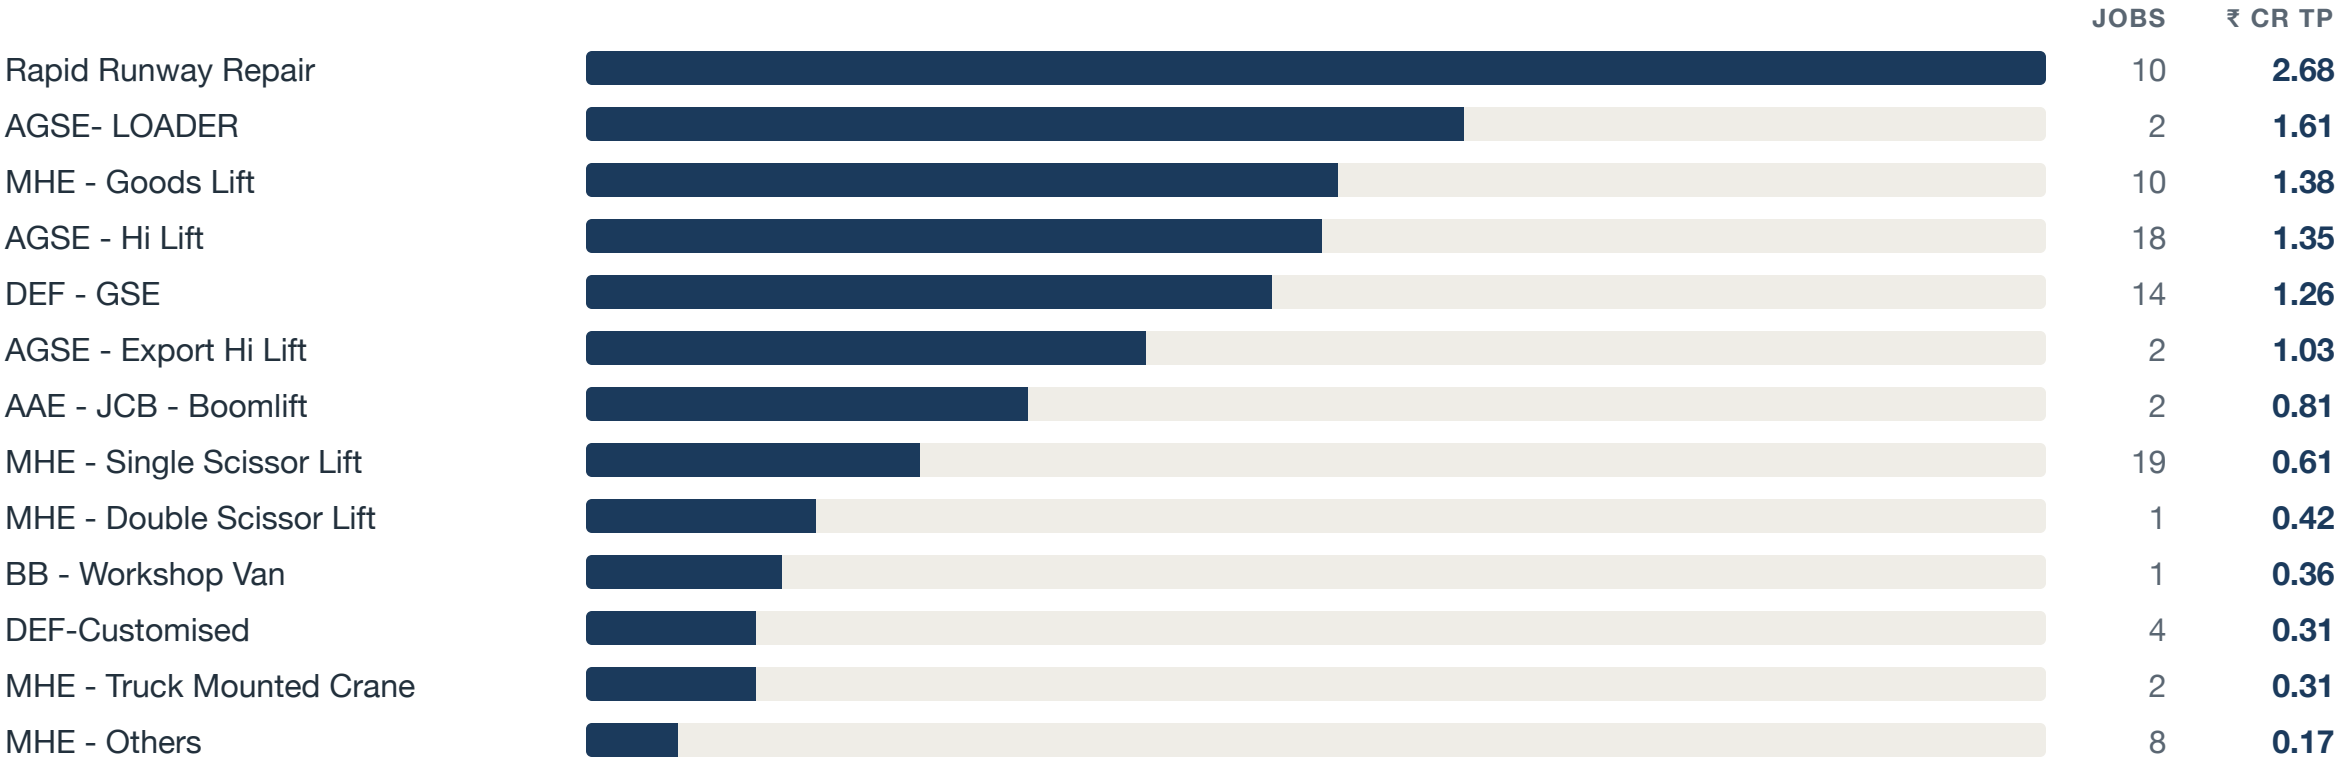

Ordered by throughput — what the company actually earns on a job, rather than what it invoices. The top 8 of 18 families carry four-fifths of it. 13 are shown; the 5 left off come to 12 jobs and ₹0.25 Cr between them.

KITTING AGAINST PRODUCTION

Genie · as at 18-08-2026

Where the money is sitting on the floor

READY TO FINISH — 12 JOBS

₹1.33 Cr

60%+ kitted and 60%+ built

Bought, made, nearly out. This is the throughput closest to being earned — and the smaller of the two piles.

KITTED, NOT MOVING — 19 JOBS

₹4.32 Cr

60%+ kitted, under 40% built

The material is bought and sitting on the floor. Nothing is being earned against it, and it is worth three times the ready pile.

THE BIGGEST STALLED JOBS

2541 Afcon - Truck mounted Scissor lift - 1.5T - Maldives · kit 60% / built 0% · **0.42 Cr**
2599 Self Propelled Articulating Boom - Airbus - Spain -… · kit 100% / built 0% · **0.41 Cr**
2600 Self Propelled Articulating Boom - Airbus - Spain -… · kit 100% / built 0% · **0.41 Cr**
2487 RRR-TIPL-IAF#75(IMDM - I / 1592) · kit 60% / built 10% · **0.30 Cr**
2489 RRR-TIPL-IAF#77(IMDM - I / 1594) · kit 60% / built 10% · **0.30 Cr**
2490 RRR-TIPL-IAF#78(IMDM - I / 1595) · kit 60% / built 10% · **0.30 Cr**
2486 RRR-TIPL-IAF#74(IMDM - I / 1591) · kit 60% / built 10% · **0.30 Cr**
2488 RRR-TIPL-IAF#76(IMDM - I / 1593) · kit 60% / built 10% · **0.30 Cr**
2471 RRR-TIPL-Navy#61(IMDM - II / 1806) · kit 60% / built 10% · **0.27 Cr**
2473 RRR-TIPL-Navy#63(IMDM - II / 1808) · kit 60% / built 10% · **0.27 Cr**

and 9 more, 1.05 Cr between them

THE NEAR SIDE OF THE LINE

Genie · as at 18-08-2026

The 12 jobs closest to going out

Job	What it is	Kit	Built	₹ Cr	Due	Open tasks
2114	Spruce Engineering Co - K-Loader - Vishakhapa…	70%	70%	0.81	31-08	6
2539	8 BRD - TMC - Chennai - #1	90%	90%	0.15	25-08	—
2540	8 BRD - TMC - Chennai - #2	90%	90%	0.15	25-08	—
2517	EIH - HL-FC - 6.3 - #6 of 6 - MUM	100%	60%	0.08	25-08	—
2575	Fuel Bowsers 990 Ltr Karnavati Aviation (Adan…	90%	60%	0.07	21-08	2
2120	Spruce Eng - Container Cradle Frame 40 FT - V…	100%	70%	0.02	31-08	—
2116	Spruce Engineering co - Portable Loading Ramp…	90%	80%	0.01	31-08	—
2117	Spruce Engineering co - Portable Loading Ramp…	90%	80%	0.01	31-08	—
2588	Verni Hydrocarbon- Vayu TL- 350KG- 1Q	100%	70%	0.01	31-08	—
2266	Spruce Engineering Co - Container Cradle Fram…	100%	90%	0.00	31-08	—
2268	Spruce Engineering Co - Container Cradle Fram…	100%	90%	0.00	31-08	—
2267	Spruce Engineering Co - Container Cradle Fram…	100%	80%	0.00	31-08	—

WHAT IS STILL OPEN ON THEM

2114 · Material · MT · due 14-08 · **ESCALATED L1** — electrical dash board items

2114 · Projects · RJ · due 18-08 · **ESCALATED L1** — Braking system finalization

2114 · Material · MT · due 19-08 — Quick release pins for railings

2114 · Material · MT · due 19-08 — Material: Chassis / base frame steel

2114 · Material · MT · due 20-08 — Radiator hoses

2114 · Design · RJ · due 20-08 · **ESCALATED L3** — IIT Approval to be done

2575 · Projects · PS · due 13-08 · **ESCALATED L3** — Send nandan Mud flap Size 9" each

2575 · Design · PS · due 18-08 — Will Visit to Supplier at Thane

8 open tasks stand between these 12 jobs and the door — 6 of them on job 2114 alone.

WHAT IS BEING ESCALATED

The same problem, on job after job

59
of 105 jobs carry a project escalation

21
open tasks are escalated

7
of those sit at L3 — Management

THE OLDEST ESCALATED TASKS

2596 · L2 · PS · due 07-08 — Modification for 4 Mtr height - YCN
2596 · L2 · PS · due 07-08 — Gearbox - Motor mounting plate - AP
2560 · L3 · PG · due 08-08 — AC unit - MT
2575 · L3 · PS · due 13-08 — Send nandan Mud flap Size 9" each
2114 · L1 · MT · due 14-08 — electrical dash board items
2513 · L2 · unassigned · due 17-08 — Need manpower for scissor frame, cylinder bracket w…

AND WHAT THE JOBS THEMSELVES SAY

2114 0.81 Cr — “W32 - Design - 1. Braking System design and components release 2. Wireless remote features and controls to be p…”
2115 0.81 Cr — “W30 - Design - 1. Braking System design and components release 2. Type of camera require with features required…”
2541 0.42 Cr — “W31: Design: 1. Hyd power pack mounting: Purchase: Chassis pending.”

Read the escalation text and it is the same theme on job after job: drawings not signed off, design not released, components not frozen. The constraint is upstream of the shop floor.
