NANDAN GSE · FY2026-27

# The year, as the book stands today

Date of Report **18 August 2026**

Day 140 of 365. Everything delivered so far, plus every job on the board, comes to just over half the year's target.

SALES — ANTICIPATED

**₹50.76 Cr**

of ₹100.00 Cr target

**51% of target**

THROUGHPUT — ANTICIPATED

**₹21.24 Cr**

of ₹40.00 Cr target

**53% of target**

> **The book runs out in November.** 105 jobs on the board, none of them dated after it.

> **₹4.32 Cr is kitted and not moving.** Material bought, sitting on the floor, nothing earned against it.

> **59 of 105 jobs are escalated** — and it is the same cause on job after job.

*delivered since 1 April + every job still on the board*

SINCE 1 APRIL

Genie · as at 18-08-2026

# What has actually gone out of the door

**DELIVERED**

**₹17.18 Cr**

61 jobs · ₹8.68 Cr throughput

**PACE SAYS BY TODAY**

**₹38.36 Cr**

140 of 365 days elapsed

**BEHIND BY**


**₹21.18 Cr**

running at 45% of the pace needed

**REQUIRED RUN RATE FOR THE REST OF THE YEAR**

**₹11.20 Cr** per month in sales, with a throughput of **₹4.23 Cr** per month

*across the 225 days that remain*

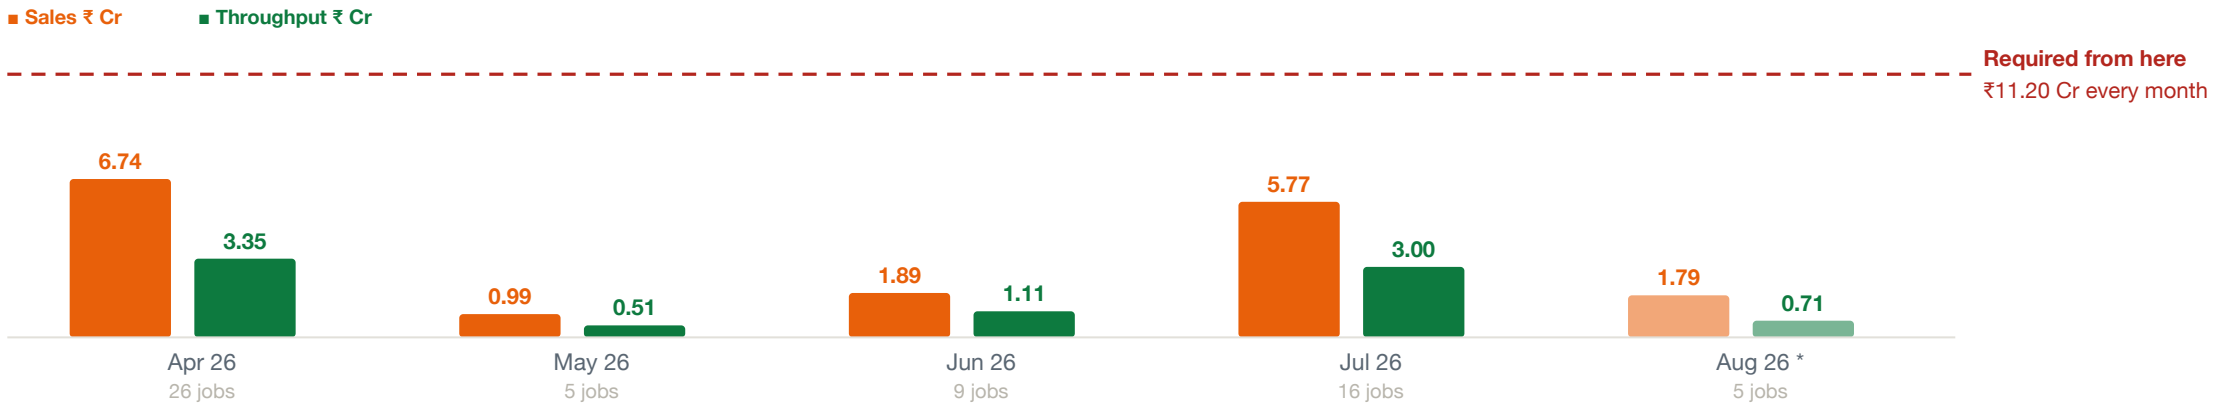



No month this year has reached the rate now required; the best of them, April, came to ₹6.74 Cr. ** Aug 26 is 18 days old, not a full month.*

THE ORDER BOOK

Genie · as at 18-08-2026

# Everything on the board runs out in November

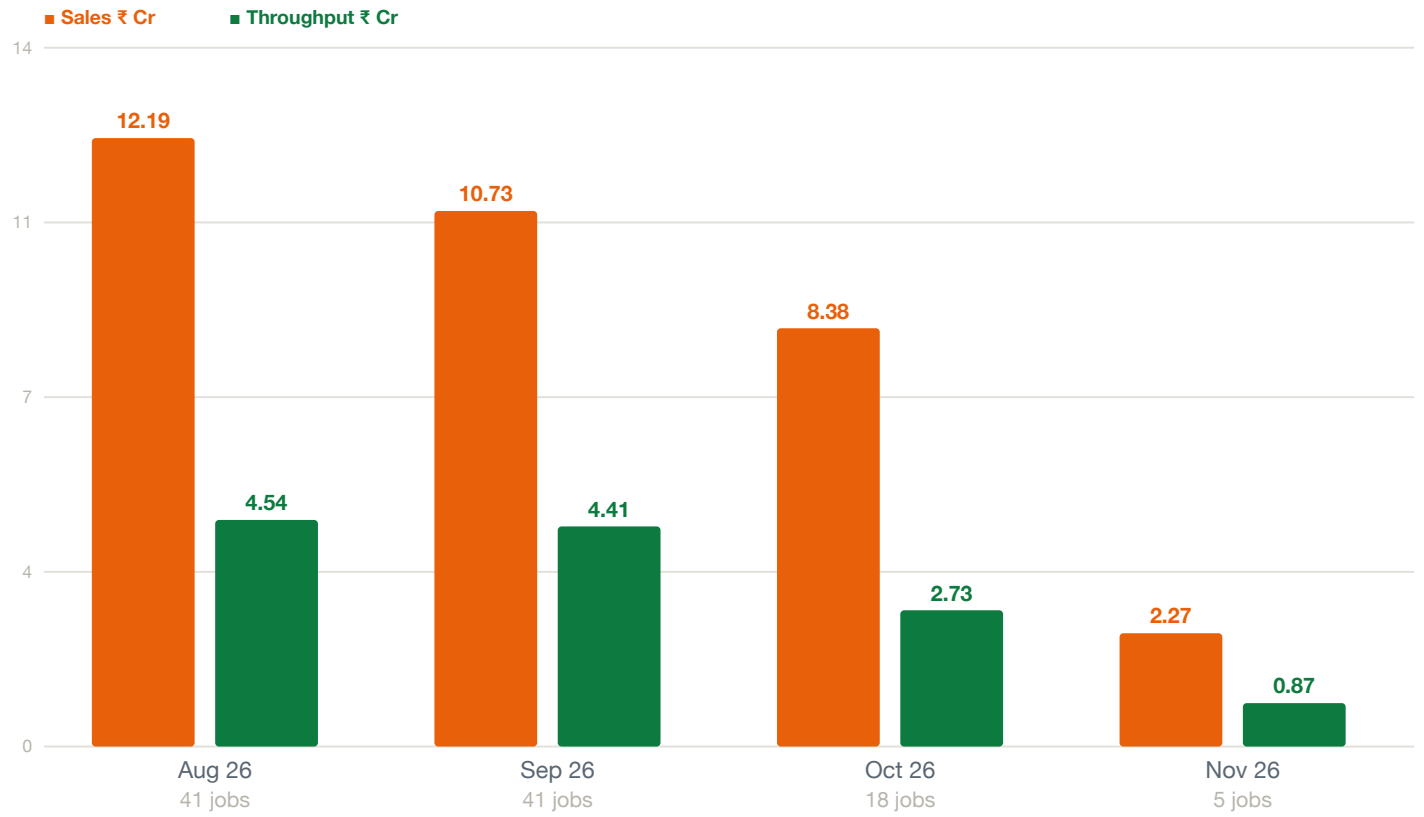


ON THE BOARD

**105 jobs**

₹33.58 Cr · ₹12.56 Cr throughput

*all of it dated August–November*

AFTER THAT

**Nothing**


Not one job on the book carries a delivery date beyond November.

**This is not a delivery problem. Even built perfectly and on time, the current book cannot reach the target — the shortfall is orders, not output.**

THE BOOK BY PRODUCT

Genie · as at 18-08-2026

# What the 105 jobs actually are

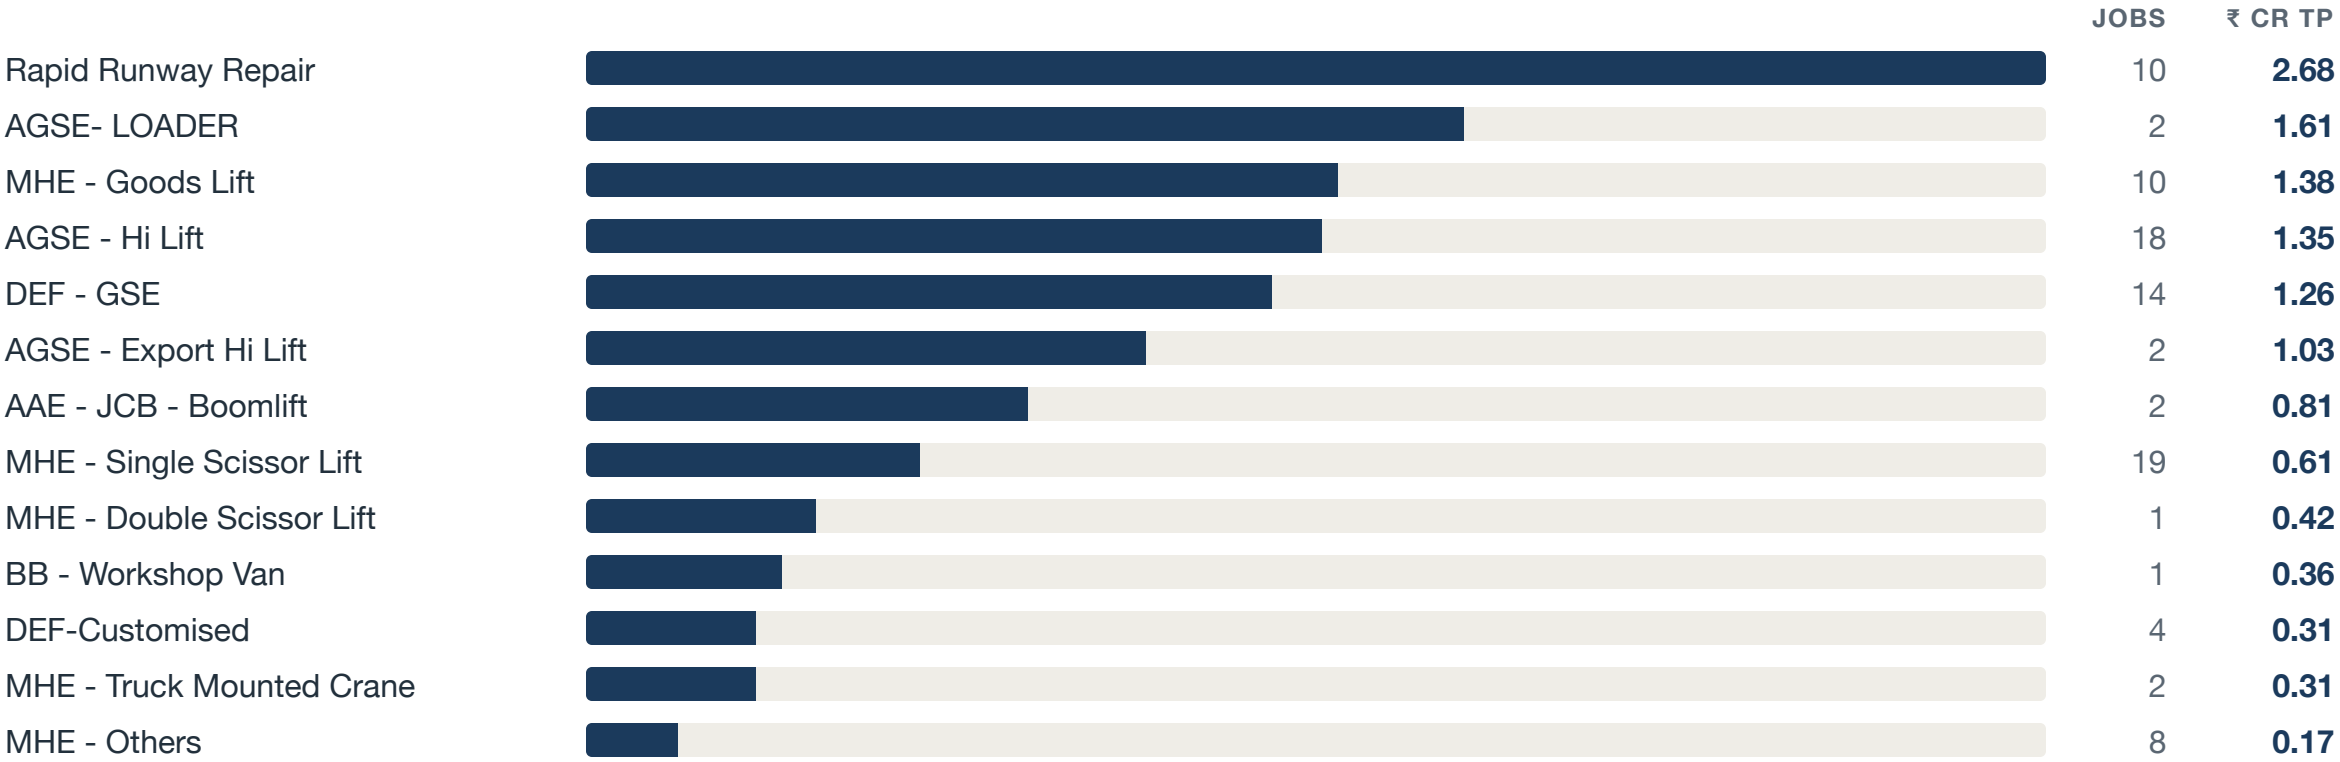


Ordered by throughput — what the company actually earns on a job, rather than what it invoices. The top 7 of 18 families carry four-fifths of it. 13 are shown; the 5 left off come to 12 jobs and ₹0.25 Cr between them.

KITTING AGAINST PRODUCTION

Genie · as at 18-08-2026

# Where the money is sitting on the floor

READY TO FINISH — 12 JOBs

## ₹1.33 Cr

**60%+ kitted and 60%+ built**

Bought, made, nearly out. This is the throughput closest to being earned — and the smaller of the two piles.

KITTED, NOT MOVING — 19 JOBs

## ₹4.32 Cr

**60%+ kitted, under 40% built**

The material is bought and sitting on the floor. Nothing is being earned against it, and it is worth 3.2 times the ready pile.

THE BIGGEST STALLED JOBS

**2541** Afcon - Truck mounted Scissor lift - 1.5T - M… · kit 60% / built 0% · **0.42 Cr**
**2599** Self Propelled Articulating Boom - Airbus - S… · kit 100% / built 0% · **0.41 Cr**
**2600** Self Propelled Articulating Boom - Airbus - S… · kit 100% / built 0% · **0.41 Cr**
**2486** RRR-TIPL-IAF#74(IMDM - I / 1591) · kit 60% / built 10% · **0.30 Cr**
**2487** RRR-TIPL-IAF#75(IMDM - I / 1592) · kit 60% / built 10% · **0.30 Cr**
**2488** RRR-TIPL-IAF#76(IMDM - I / 1593) · kit 60% / built 10% · **0.30 Cr**
**2489** RRR-TIPL-IAF#77(IMDM - I / 1594) · kit 60% / built 10% · **0.30 Cr**
**2490** RRR-TIPL-IAF#78(IMDM - I / 1595) · kit 60% / built 10% · **0.30 Cr**
**2471** RRR-TIPL-Navy#61(IMDM - II / 1806) · kit 60% / built 10% · **0.27 Cr**
**2472** RRR-TIPL-Navy#62(IMDM - II / 1807) · kit 60% / built 10% · **0.27 Cr**

and 9 more, 1.05 Cr between them

THE NEAR SIDE OF THE LINE

Genie · as at 18-08-2026

# The 12 jobs closest to going out

| Job | What it is | Kit | Built | ₹ Cr | Due | Open tasks |
|---|---|---|---|---|---|---|
| 2114 | Spruce Engineering Co - K-Loader - Vishakhapa… | 70% | 70% | 0.81 | 31-08 | 6 |
| 2539 | 8 BRD - TMC - Chennai - #1 | 90% | 90% | 0.15 | 25-08 | — |
| 2540 | 8 BRD - TMC - Chennai - #2 | 90% | 90% | 0.15 | 25-08 | — |
| 2517 | EIH - HL-FC - 6.3 - #6 of 6 - MUM | 100% | 60% | 0.08 | 25-08 | — |
| 2575 | Fuel Bowsers 990 Ltr Karnavati Aviation (Adan… | 90% | 60% | 0.07 | 21-08 | 2 |
| 2120 | Spruce Eng - Container Cradle Frame 40 FT - V… | 100% | 70% | 0.02 | 31-08 | — |
| 2116 | Spruce Engineering co - Portable Loading Ramp… | 90% | 80% | 0.01 | 31-08 | — |
| 2117 | Spruce Engineering co - Portable Loading Ramp… | 90% | 80% | 0.01 | 31-08 | — |
| 2588 | Verni Hydrocarbon- Vayu TL- 350KG- 1Q | 100% | 70% | 0.01 | 31-08 | — |
| 2266 | Spruce Engineering Co - Container Cradle Fram… | 100% | 90% | 0.00 | 31-08 | — |
| 2267 | Spruce Engineering Co - Container Cradle Fram… | 100% | 80% | 0.00 | 31-08 | — |
| 2268 | Spruce Engineering Co - Container Cradle Fram… | 100% | 90% | 0.00 | 31-08 | — |

## WHAT IS STILL OPEN ON THEM

**2575** · Projects · PS · due 13-08 · **ESCALATED L3** — Send nandan Mud flap Size 9" each

**2114** · Material · MT · due 14-08 · **ESCALATED L1** — electrical dash board items

**2114** · Projects · RJ · due 18-08 · **ESCALATED L1** — Braking system finalization

**2575** · Design · PS · due 18-08 — Will Visit to Supplier at Thane

**2114** · Material · MT · due 19-08 — Quick release pins for railings

**2114** · Material · MT · due 19-08 — Material: Chassis / base frame steel

**2114** · Material · MT · due 20-08 — Radiator hoses

**2114** · Design · RJ · due 20-08 · **ESCALATED L3** — IIT Approval to be done

**8 open tasks stand between these 12 jobs and the door — 6 of them on job 2114 alone.**

# 20 jobs, ₹2.38 Cr of throughput, and almost none of it built


| Job | Customer | Kit | Built | ₹ Cr | Due | Esc |
|---|---|---|---|---|---|---|
| 2560 | Encalm Hospitality Pvt Ltd | 60% | 0% | 0.11 | 21-08 | • |
| 2517 | EIH Limited | 100% | 60% | 0.08 | 25-08 | • |
| 2504 | EIH Limited | 80% | 40% | 0.08 | 30-08 | • |
| 2548 | Taj Sats Air Catering Lim… | 50% | 20% | 0.09 | 30-08 | • |
| 2549 | Taj Sats Air Catering Lim… | 80% | 50% | 0.09 | 30-08 | • |
| 2513 | EIH Limited | 60% | 20% | 0.08 | 31-08 | • |
| 2514 | EIH Limited | 100% | 55% | 0.08 | 31-08 | • |
| 2561 | Encalm Hospitality Pvt Ltd | 60% | 0% | 0.11 | 01-09 | • |
| 2550 | Taj Sats Air Catering Lim… | 10% | 0% | 0.09 | 07-09 | • |
| 2551 | Taj Sats Air Catering Lim… | 10% | 0% | 0.09 | 10-09 | • |
| 2505 | EIH Limited | 50% | 5% | 0.08 | 12-09 | • |
| 2555 | Taj Sats Air Catering Lim… | 60% | 15% | 0.09 | 15-09 | • |
| 2515 | EIH Limited | 50% | 5% | 0.08 | 18-09 | • |
| 2516 | EIH Limited | 50% | 5% | 0.08 | 22-09 | • |

and 6 more jobs, 1.14 Cr between them

**12 jobs**
at 50%+ kitted

**3 jobs**
at 50%+ built

**15 of 20**
escalated

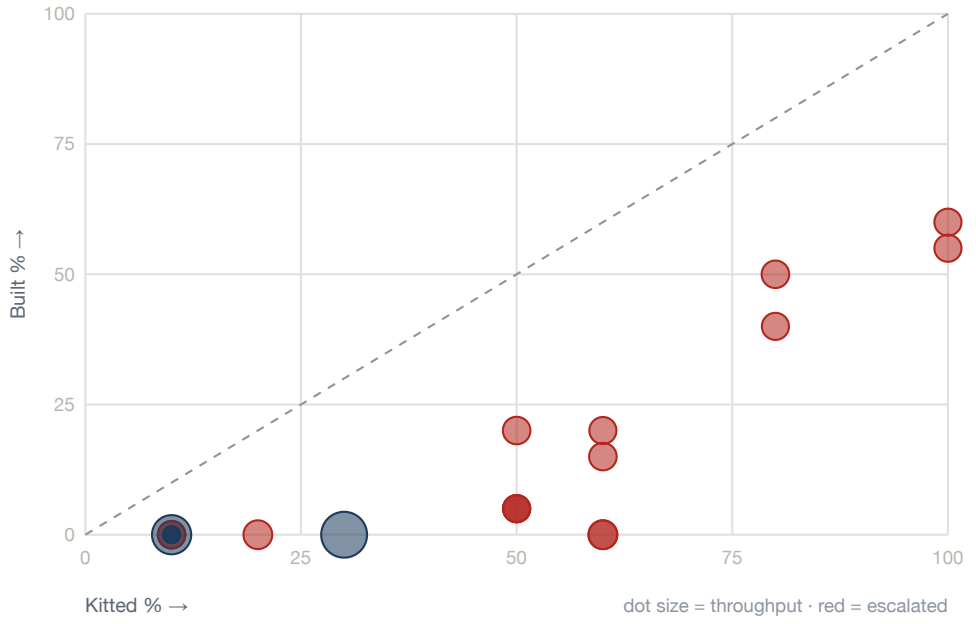


## WHO IS WAITING

**Malawi Catering Services Limi…** · 1 job · 0.65 Cr
**EIH Limited** · 7 jobs · 0.56 Cr
**Taj Sats Air Catering Limited** · 5 jobs · 0.45 Cr
**DrukAir Corporation Limited** · 1 job · 0.38 Cr
**Encalm Hospitality Pvt Ltd** · 3 jobs · 0.33 Cr

**16 Hi Lifts went out this year, worth ₹6.30 Cr. The 20 still on the board are ₹2.38 Cr of throughput sitting almost entirely un-built, and 3 jobs (2620, 2621, 2622) carry no order value yet — they are counted as jobs here but not as money.**

WHAT IS BEING ESCALATED

# The same problem, on job after job

**59**
of 105 jobs carry a project escalation

**21**
open tasks are escalated

**6**
of those sit at L3 — Management

### THE OLDEST ESCALATED TASKS

**2596** · L2 · PS · due 07-08 — Gearbox - Motor mounting plate - AP
**2596** · L2 · PS · due 07-08 — Modification for 4 Mtr height - YCN
**2575** · L3 · PS · due 13-08 — Send nandan Mud flap Size 9" each
**2114** · L1 · MT · due 14-08 — electrical dash board items
**2541** · L1 · MT · due 17-08 — MS chequered plate
**2513** · L2 · unassigned · due 17-08 — Need manpower for scissor frame, cylinder bracket work

### AND WHAT THE JOBS THEMSELVES SAY

**2114** 0.81 Cr — “W32 - Design - 1. Braking System design and components release 2. Wireless remote features and controls to be p…”
**2115** 0.81 Cr — “W30 - Design - 1. Braking System design and components release 2. Type of camera require with features required…”
**2541** 0.42 Cr — “W31: Design: 1. Hyd power pack mounting: Purchase: Chassis pending.”

**Read the escalation text and it is the same theme on job after job: drawings not signed off, design not released, components not frozen. The constraint is upstream of the shop floor.**
